ID		Task Name	Duration	% Complete	Start	Finish
0		**Mt. San Jacinto District Wireless Upgrade 6917**	**121 days**	**20%**	**Thu 4/27/17**	**Tue 10/17/17**
1	✓	**Planning**	**24 days**	**100%**	**Thu 4/27/17**	**Wed 5/31/17**
2	✓	NTP for Project issued to Contractor	1 day	100%	Thu 4/27/17	Thu 4/27/17
3	✓	Project Kickoff Meeting with Contractor's Project Team and	1 day	100%	Mon 5/8/17	Mon 5/8/17
4	✓	Review and Approve Project work plan submitted by	0 days	100%	Mon 5/8/17	Mon 5/8/17
5	✓	**Pre-Construction Deliverables**	**17 days**	**100%**	**Mon 5/8/17**	**Wed 5/31/17**
6	✓	Project Team Contact Sheet	1 day	100%	Mon 5/8/17	Mon 5/8/17
7	✓	Construction Team Clearance Information	1 day	100%	Mon 5/8/17	Mon 5/8/17
8	✓	Material Lists	1 day	100%	Mon 5/8/17	Mon 5/8/17
9	✓	Data / Cut Sheets	1 day	100%	Mon 5/8/17	Mon 5/8/17
10	✓	Procurement	10 days	100%	Tue 5/9/17	Mon 5/22/17
11		**Vector - Project Deployment & Execution**	**104 days**	**10%**	**Mon 5/22/17**	**Tue 10/17/17**
12		**Mt San Jacinto College**	**53 days**	**22%**	**Mon 5/22/17**	**Fri 8/4/17**
13		**Phase I - Construction**	**52 days**	**24%**	**Mon 5/22/17**	**Thu 8/3/17**
14	✓	Site Survey/ Pathway Verification	4 days	100%	Mon 5/22/17	Thu 5/25/17
15		Pathway Install	12 days	75%	Fri 5/26/17	Tue 6/13/17
16		Copper Installation	10 days	0%	Wed 6/14/17	Tue 6/27/17
17		Copper Termination Station Side	5 days	0%	Wed 6/21/17	Tue 6/27/17
18		Copper Termination Cabinet Side	6 days	0%	Wed 6/28/17	Thu 7/6/17
19		Copper Certification	3 days	0%	Fri 7/7/17	Tue 7/11/17
20		Indoor AP installation	5 days	0%	Wed 7/12/17	Tue 7/18/17
21		Outdoor AP installation	6 days	0%	Wed 7/19/17	Wed 7/26/17
22		AP Demo	2 days	0%	Thu 7/27/17	Fri 7/28/17
23		QA/QC Walk (Verify completed installation)	1 day	0%	Mon 7/31/17	Mon 7/31/17
24		Test & Acceptance Process	1 day	0%	Thu 8/3/17	Thu 8/3/17
25		**Project Closeout Deliverables**	**2 days**	**0%**	**Thu 8/3/17**	**Fri 8/4/17**
26	✓	- Drawings: As-Builds Drawings	0 days	100%	Thu 8/3/17	Thu 8/3/17
27		- Warranties: Copper	1 day	0%	Fri 8/4/17	Fri 8/4/17
28		- Copper Test Results in both hard & soft copies	1 day	0%	Fri 8/4/17	Fri 8/4/17
29		- Letter of Completion to Vector Resources	1 day	0%	Fri 8/4/17	Fri 8/4/17
30		**Mt San Jacinto College Menifee Campus**	**47 days**	**0%**	**Mon 7/31/17**	**Wed 10/4/17**
31		**Phase I - Construction**	**46 days**	**0%**	**Mon 7/31/17**	**Tue 10/3/17**
32		Site Survey/ Pathway Verification	4 days	0%	Mon 7/31/17	Thu 8/3/17
33		Pathway Install	10 days	0%	Fri 8/4/17	Thu 8/17/17
34		Copper Installation	10 days	0%	Fri 8/18/17	Thu 8/31/17
35		Copper Termination Station Side	5 days	0%	Fri 8/25/17	Thu 8/31/17
36		Copper Termination Cabinet Side	6 days	0%	Fri 9/1/17	Mon 9/11/17
37		Copper Certification	3 days	0%	Tue 9/12/17	Thu 9/14/17
38		Indoor AP installation	5 days	0%	Fri 9/15/17	Thu 9/21/17
39		Outdoor AP installation	3 days	0%	Fri 9/22/17	Tue 9/26/17
40		AP Demo	2 days	0%	Wed 9/27/17	Thu 9/28/17

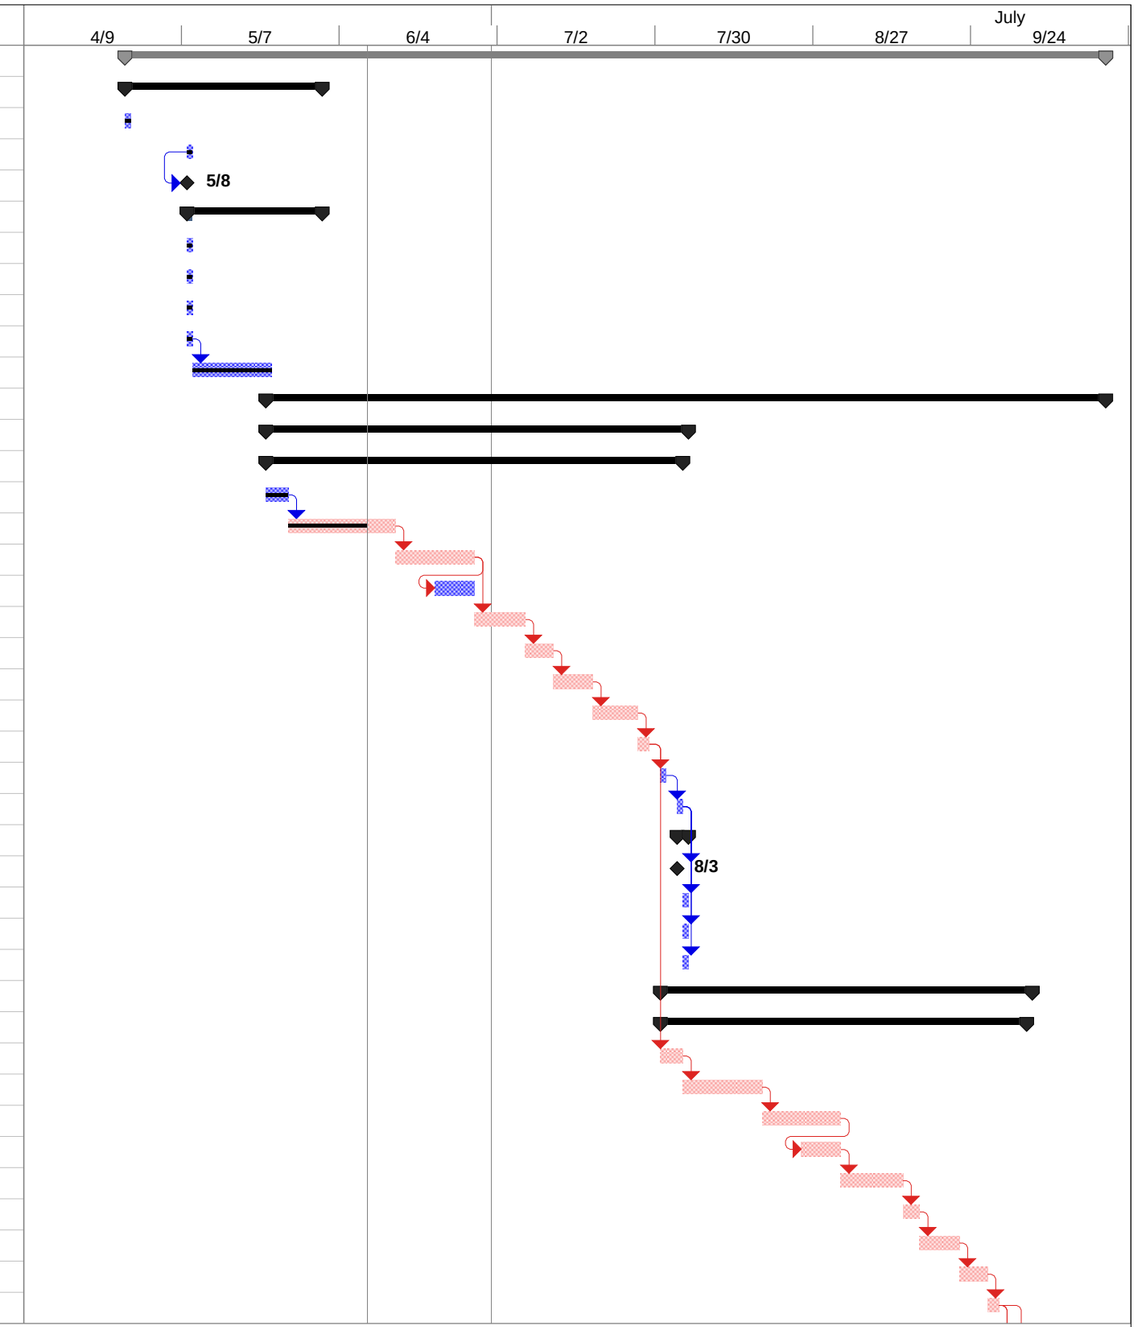

Project: Mt. San Jacinto District Wirele
Date: Fri 6/9/17

Task		External Tasks		Inactive Summary		Start-only		Deadline	
Split		External Milestone		Manual Task		Finish-only			
Milestone		Inactive Task		Duration-only		Critical			
Summary		Inactive Task		Manual Summary Rollup		Critical Split			
Project Summary		Inactive Milestone		Manual Summary		Progress			

ID		Task Name	Duration	% Complete	Start	Finish
41		QA/QC Walk (Verify completed installation)	2 days	0%	Fri 9/29/17	Mon 10/2/17
42		Test & Acceptance Process	1 day	0%	Tue 10/3/17	Tue 10/3/17
43		**Project Closeout Deliverables**	**1 day**	**0%**	**Wed 10/4/17**	**Wed 10/4/17**
44		- Drawings: As-Builds Drawings	1 day	0%	Wed 10/4/17	Wed 10/4/17
45		- Warranties: Copper	1 day	0%	Wed 10/4/17	Wed 10/4/17
46		- Copper Test Results in both hard & soft copies	1 day	0%	Wed 10/4/17	Wed 10/4/17
47		- Letter of Completion to Vector Resources	1 day	0%	Wed 10/4/17	Wed 10/4/17
48		**Temecula Education Complex**	**13 days**	**0%**	**Fri 9/29/17**	**Tue 10/17/17**
49		**Phase I - Construction**	**12 days**	**0%**	**Fri 9/29/17**	**Mon 10/16/17**
50		Site Survey/ Pathway Verification	1 day	0%	Fri 9/29/17	Fri 9/29/17
51		Pathway Install	2 days	0%	Mon 10/2/17	Tue 10/3/17
52		Copper Installation	2 days	0%	Wed 10/4/17	Thu 10/5/17
53		Copper Termination Station Side	1 day	0%	Wed 10/4/17	Wed 10/4/17
54		Copper Termination Cabinet Side	1 day	0%	Fri 10/6/17	Fri 10/6/17
55		Copper Certification	1 day	0%	Mon 10/9/17	Mon 10/9/17
56		Indoor AP installation	1 day	0%	Tue 10/10/17	Tue 10/10/17
57		AP Demo	1 day	0%	Wed 10/11/17	Wed 10/11/17
58		QA/QC Walk (Verify completed installation)	1 day	0%	Thu 10/12/17	Thu 10/12/17
59		Test & Acceptance Process	1 day	0%	Mon 10/16/17	Mon 10/16/17
60		**Project Closeout Deliverables**	**1 day**	**0%**	**Tue 10/17/17**	**Tue 10/17/17**
61		- Drawings: As-Builds Drawings	1 day	0%	Tue 10/17/17	Tue 10/17/17
62		- Warranties: Copper	1 day	0%	Tue 10/17/17	Tue 10/17/17
63		- Copper Test Results in both hard & soft copies	1 day	0%	Tue 10/17/17	Tue 10/17/17
64		- Letter of Completion to Vector Resources	1 day	0%	Tue 10/17/17	Tue 10/17/17

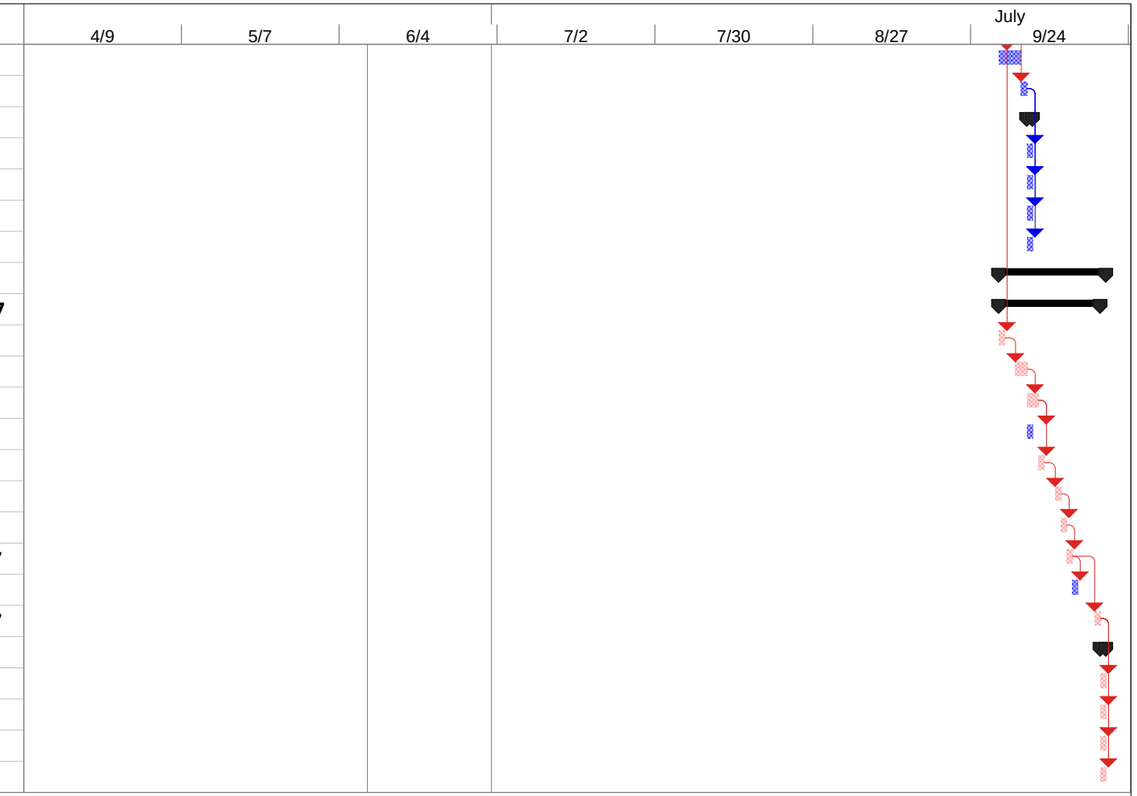

Project: Mt. San Jacinto District Wirele
Date: Fri 6/9/17

Task		External Tasks		Inactive Summary		Start-only		Deadline	
Split		External Milestone		Manual Task		Finish-only			
Milestone		Inactive Task		Duration-only		Critical			
Summary		Inactive Task		Manual Summary Rollup		Critical Split			
Project Summary		Inactive Milestone		Manual Summary		Progress			
